MISSISSIPPI
ADHS 2007 COST-TO-COMPLETE ESTIMATE

Mississippi has two ADHS corridors with a total of 127.9-miles (including 10.4 ineligible miles). Eligible mileage is 90 percent complete and open to traffic, and an additional 6 percent is in the stage construction phase. The 2007 cost-to-complete estimate for Mississippi's ADHS corridors is $79.7 million (state and federal funds). The federal share of the cost to complete is $50.3 million.

Mississippi has $45.7 million in federal funds available, including funds from ADHS apportionments, earmarks in TEA-21, allocations under various appropriations acts, and future apportionments authorized for FY 2008 and FY 2009 under SAFETEA-LU.

Mississippi needs $4.6 million in additional federal funds to complete its portion of the ADHS.

Status of Completion of ADHS Miles in Mississippi, as of September 30, 2006
(Eligible Miles: 117.5)

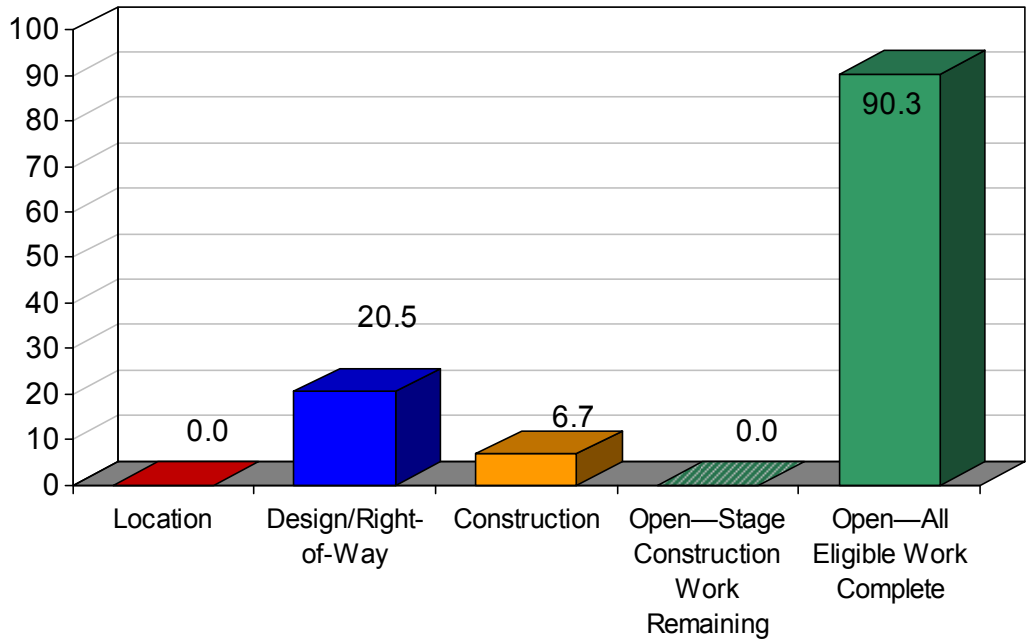

Corridor X

Corridor X is complete and open to traffic. The corridor extends 9.1 miles from Corridor V to the Alabama state line.

Corridor V

Corridor V extends 118.8 miles (including 10.4 ineligible miles) from I-55 to the Alabama state line. The estimated cost to complete Corridor V is $79.7 million. *As the result of a shift of eligibility approved on July 19, 2001, ADHS funding on a segment from the Pontotoc and Line County line to SR 145 is limited to $27,860,360 (in 2005 dollars).*

Remaining work in the 2007 estimate is for the four-lane construction of a 9.8-mile section of SR 6 in a new location west of Tupelo, and 4.1 miles of an 11.4-mile section on a new location from SR 25 to the Alabama state line. Stage construction (grading, drainage and bridges) is scheduled to start in FY 2007.

Appalachian Development Highway System
MISSISSIPPI

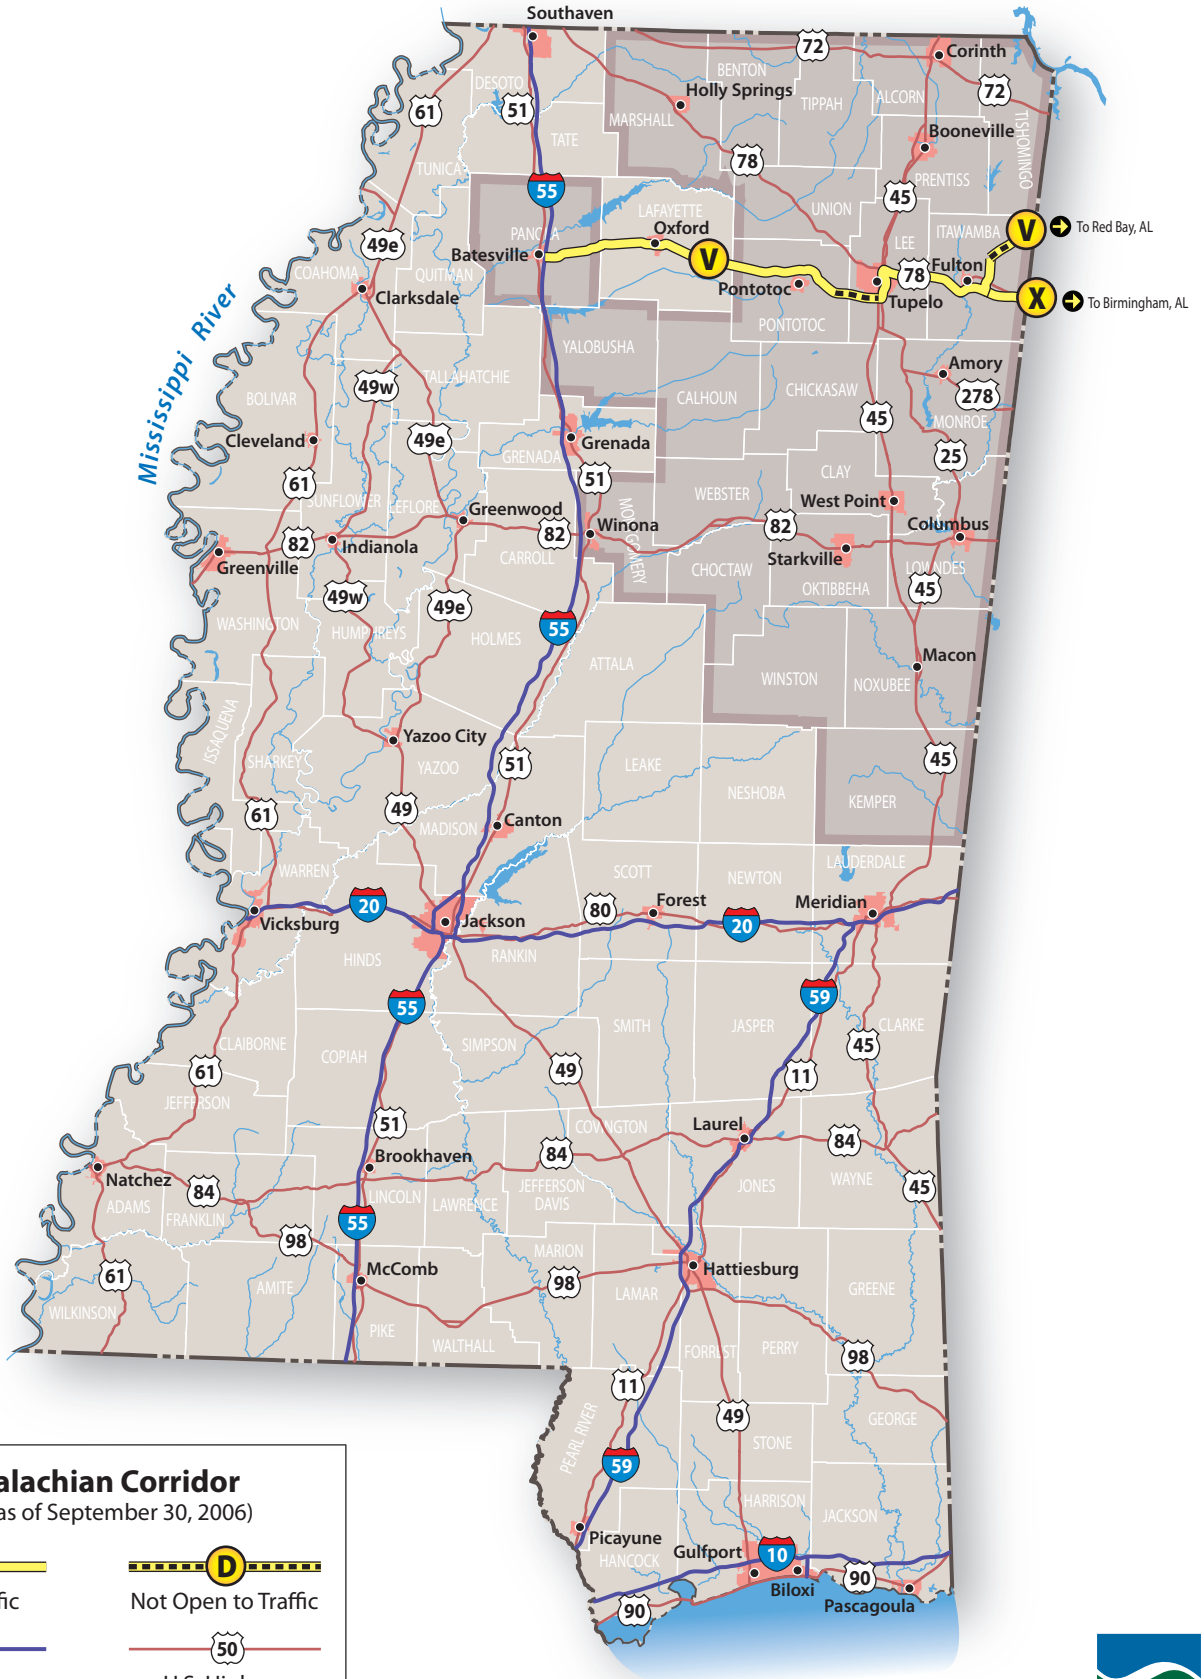

ARC
APPALACHIAN REGIONAL COMMISSION
