# STATUS OF CORRIDORS IN ALABAMA

## Appalachian Development Highway System (ADHS)
## Alabama Corridors as of September 30, 2012

### Summary

| | |
|---|---|
| Total Number of ADHS Miles: | 308.4 miles |
| Number of ADHS Miles Eligible for Funding: | 295.7 miles |
| Number of ADHS Completed Miles: | 152.4 miles |
| Miles Remaining Stage Construction (Open to Traffic): | 58.6 miles |
| Miles Under Construction: | 17.8 miles |
| Miles in Design/Right-of-Way Stage: | 23.6 miles |
| Miles in Location Study Stage: | 43.3 miles |

Total ADHS-Funded Obligations To Date
(Federal and State): $1,801.1 million

Estimated Cost to Complete, Federal and State Funds: $3,254.7 million
(as of September 30, 2011)

| | |
|---|---|
| Corridor V: | $156.2 million |
| Corridor X: | $132.1 million |
| Corridor X1: | $2,966.4 million |

### Federal Funding for Alabama Corridors in Fiscal Year 2012

In fiscal year FY 2012, Alabama was apportioned $109,694,169 from the Surface Transportation Extension Act of 2011, Part II, for use on their ADHS Corridors.

### Fiscal Year 2012 Obligations

During fiscal year 2012, Alabama obligated a total of $3.0 million federal funds on the ADHS. This included $4.6 million from the Surface Transportation Extension Act of 2010, $4,191 from SAFETEA-LU funds, $577,664 de-obligated from TEA-21 funds, $523,716 de-obligated from TEA-21 Extension Acts, $92,805 from the Water and Energy Appropriation Acts, $75,963 de-obligated from the FY 2001 DOT Appropriation Act, $393,160 de-obligated from the FY 2003 Omnibus Appropriations Act, $39,390 de-

obligated from the FY 2004 Consolidated Appropriations Act and $45,000 de-obligated from the FY 1999 Omnibus Appropriations Act.

## Status of Corridors

**Corridor V** (State Route 24, I-565, State Routes 2 and 3, U.S. 72)
Corridor V enters Alabama at the Mississippi state line near Red Bay and runs through Huntsville to the Tennessee state line near Bridgeport. The total length of the corridor in Alabama is 145.4 miles.

| | |
|---|---|
| Authorized for ADHS Funding | 135.4 miles |
| All Eligible Work Complete | 93.7 miles |
| Remaining Stage Construction | 25.0 miles |
| Construction Under Way | 14.8 miles |
| Design & ROW Stage | 1.2 miles |
| Location Study Stage | 0.7 miles |

Projects currently under way on Corridor V in Alabama include:

- Construction on a 5.6-mile bypass at Red Bay from the Mississippi State line to SR-247.
- Construction on a 7.8-mile section from SR-247 to Dempsey.
- Construction on a 7.3-mile section from Dempsey to 3 miles west of Russellville.
- Construction on a 1.4-mile section in Decatur.
- Final Design on a 2.9-mile section east of Huntsville.

**Corridor X** (State Route 4, U.S. 78, State Route 3, U.S. 31)
Corridor X enters the state at the Mississippi state line near Weston and ends at I-65/I-59 at Birmingham. The total length of the corridor in Alabama is 98.0 miles.

| | |
|---|---|
| Authorized for ADHS Funding | 95.3 miles |
| All Eligible Work Complete | 58.7 miles |
| Remaining Stage Construction | 33.6 miles |
| Construction Under Way | 3.0 miles |

Projects currently under way on Corridor X in Alabama include:

- Construction underway from CR 105 in Jefferson County to 400 feet west of I-65 in Jefferson County
- Construction underway on the 2nd phase of the Corridor X/I-65 interchange
- Final design on the section from 1.4 miles west of I-65 to the I-65/US 31 Interchange at Birmingham
- Final design on the ultimate paving from SR118 to West of Industrial Parkway near Jasper

**Corridor X1** (Birmingham Northern Beltline)

Section 123 of the FY 2004 Consolidated Appropriations Act added Corridor X1 in Alabama to ADHS. Corridor X1 extends approximately 65 miles along the alignment of the planned Birmingham Northern Beltline from I-20/59, in the vicinity of I-495 southwest of Birmingham, and extending northward crossing SR 269 and Corridor X and continuing eastward crossing I-65, US 31, SR 79, SR75, I-59, US 11, US 411 and connecting to I-20 to the east of Birmingham.

| | |
|---|---|
| Authorized for ADHS Funding | 65.0 miles |
| Design & ROW Stage: | 22.4 miles |
| Location Study Stage: | 42.6 miles |

Project currently under way on Corridor X1 in Alabama include:

- Design and right-of-way acquisition unde rway on a 3.4-m ile section from west of SR 79 to east of SR 75.

# Appalachian Development Highway System
# ALABAMA

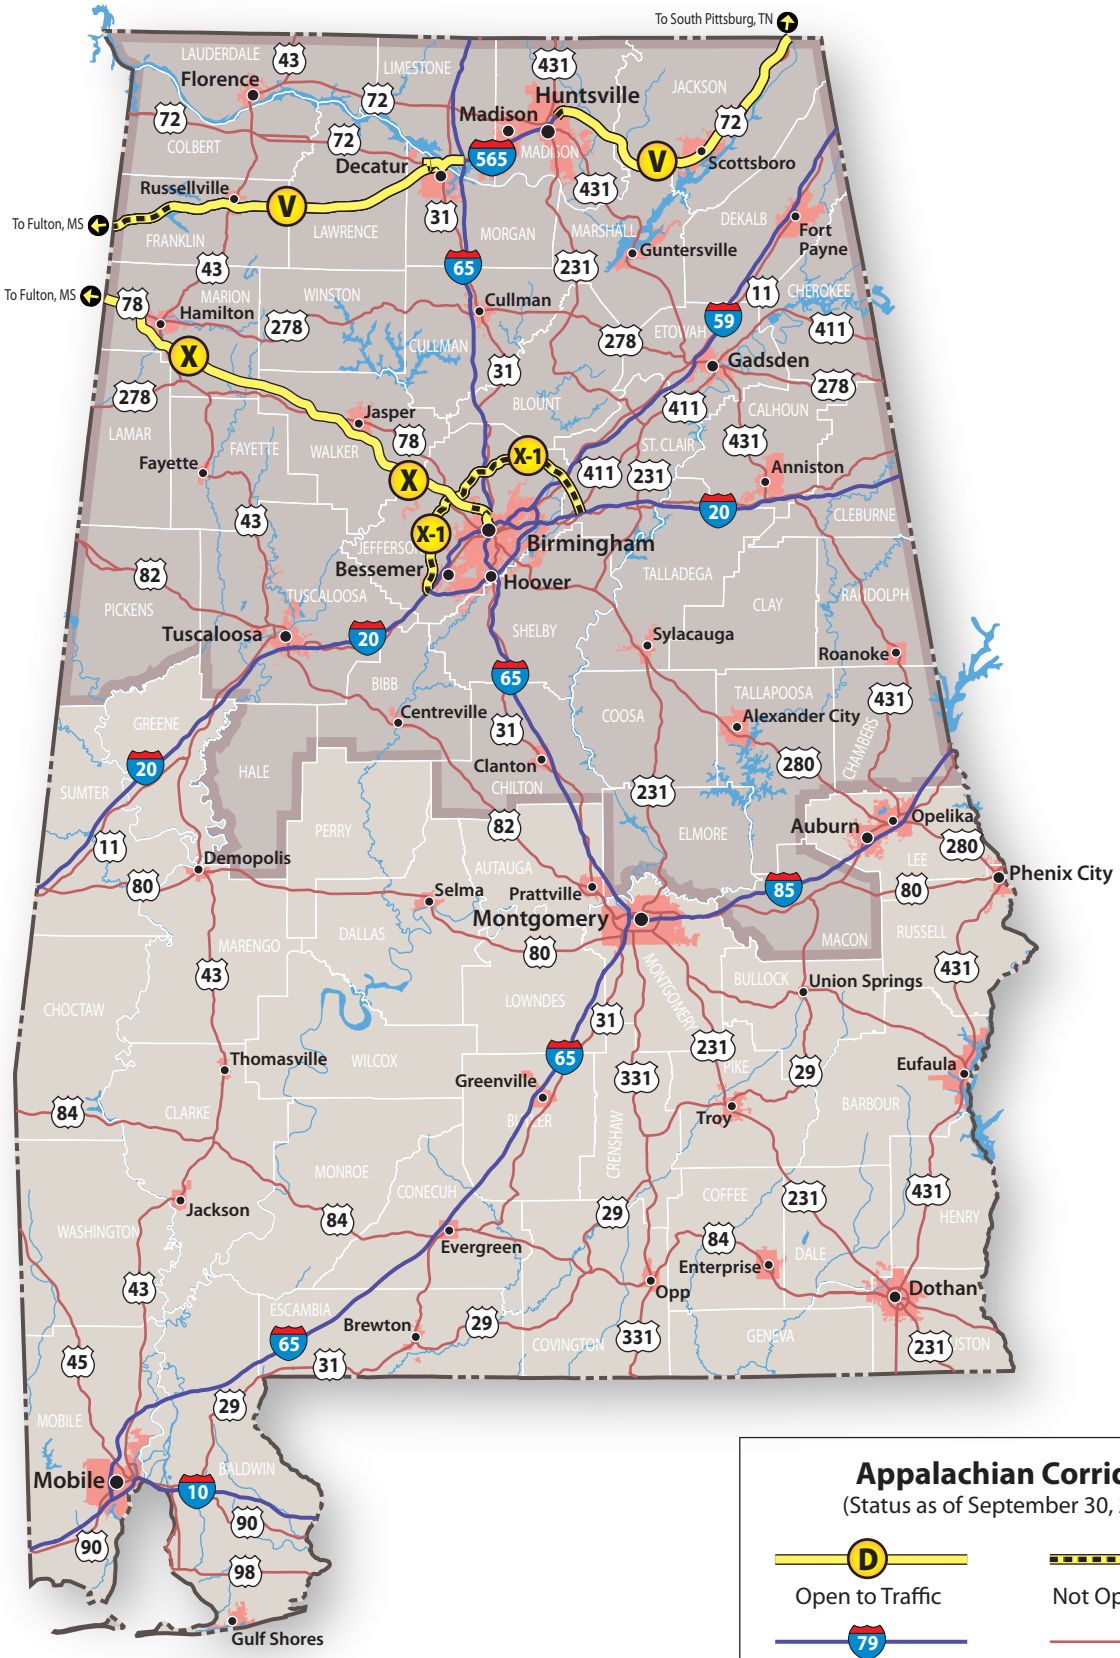


## Appalachian Corridor
(Status as of September 30, 2012)

- Open to Traffic
- Not Open to Traffic
- Interstate Highway
- U.S. Highway
- Populated Place
- Appalachian Region

APPALACHIAN REGIONAL COMMISSION
